


Mobile App Testing Effort Estimation

Greetings from **testbytes!**

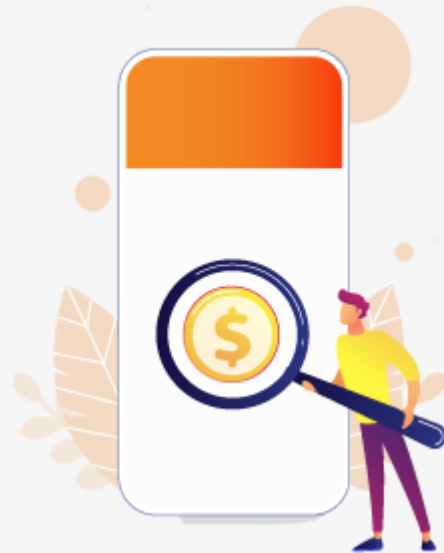

Dear MY NAME iSO,

Thank you for using our cost estimation calculator.

Estimation for your requirement is presented in 3 different break-up for better understanding

- 1) First break-up is based on planning and execution of tests
- 2) Second is the effort involved in testing various modules of your app
- 3) Third is the effort estimation of types of testing that is going to be used on your app

Specifications

User Preferences

Domain	Fashion
Platforms	IOS
No: of Screens	5
No: of Devices	10
No: of external Interface	5-10
Default Type of Testing	Functional Testing,Usability Testing,Compatibility Testing
Type of Testing (Opted)	Compatibility Testing,Beta Testing

How Complex	Complex
No: of Cycles	4
No: of Test Cases	178

Test Execution Effort Breakdown

Test Preparation Effort




Test Execution Effort

Cycles	Test Preparation	Test Execution	Defect Reporting	Retesting (if testcase failed)
1	13.00	45.96	22.24	14.83
2	13.00	45.96	11.12	0.62
3	13.00	34.84	11.12	0.31
4	13.00	29.28	5.56	0.15
Total	52.00	156.00	50.00	16.00
Total Test Cycle Execution Efforts (in hrs)				274
Compatibility Testing (in hrs) (10 Devices)				24
Total Efforts (in hrs)				459

Effort involved in testing various Modules

Modules	Efforts (Hrs.)
Screen Design	41
Android App	99
iOS App	66
Other Features	3
Database	3
Webservices	41
Admin Panel	22
Total	274

Effort involved in types of testing

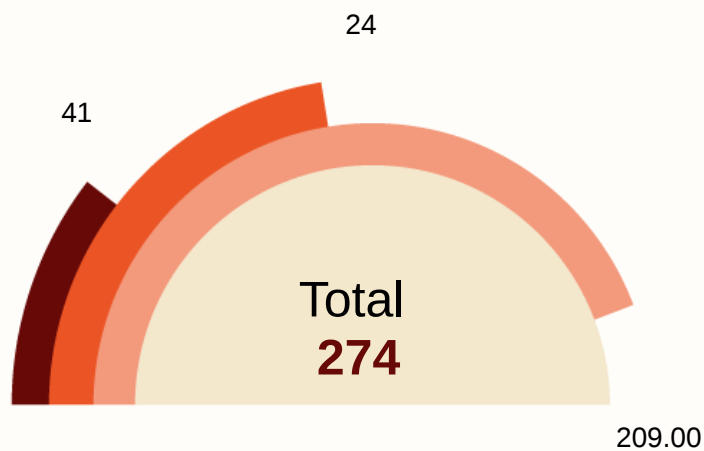

Functional Testing 209.00

Usability Testing 41

Compatibility Testing

Timeline 3 Month

Total effort is

274 Hrs

Total amount is

86,297 - 304,204 INR

* The cost has been generated by our in-house system with 85-95% accuracy.
Variations can happen owing to various factors.

Type of Testing (opted)		Efforts (Hrs.)
Compatibility Testing, Beta Testing		
Automation Testing		
Testcase Scenario	Automation Script Effort	Script Execution Effort
150.00	784.33	24.9
<p>* Test Scenario for automation is based on the existing ones. So, effort is excluded from the automation effort calculation.</p>		

Apart from your chosen types of testing, listed below are the effort involved in other types to ensure that your product is as robust as it can get.

If you wish to know why you need them Read [Here](#)

Type of Testing (optional)	Efforts (Hrs.)
Beta Testing	120
Localisation Testing	120

To ensure maximum stability, security and scalability your app it must go other forms of testing (mentioned at the estimation part).

If you wish to opt for other types of testing the estimated cost,effort and timeline would be,

Expected Timeline	Overall Effort	Overall Cost
2.5 Months	658 hrs	164,430 - 712,531 INR

If you have any query regarding the estimation feel free to contact us at



www.testbytes.net



+1 929 552 0053



+918113865000

- We are now **45K+** on **LinkedIn**

[Join us](#)
